


HCPS PROJECT PROGRESS REPORT

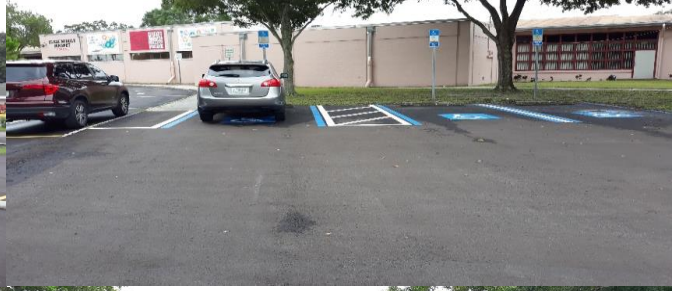

PROJECT INFORMATION: Before During After

Name: Sligh - Repave Parking Lot

Address: 2011 East Sligh Avenue

City/State/Zip: Tampa, FL 33610

District Project Number: **100070**

PROJECT DIRECTORY:

HCPS Department: Sites and Utilities

HCPS Representative: Mike Busciglio

PROJECT OVERVIEW: (A=Actual, P=Projected)

	Date	(A/P)
Project Start:	05/07/19	A
Inspection/Task: Mill Bus Ramp	05/07/19	A
Inspection/Task: Pave Bus Ramp	05/10/19	A
Inspection/Task: Mill Parking	06/17/19	A
Inspection/Task: Pave Parking	06/20/19	A
Inspection/Task: Stripe Parking	07/19/19	A
Final Completion:	07/22/19	A
Total Project Duration:	76	Days

Contractor / Bid-Vendor:	Alto Construction
Contractor / Bid-Vendor:	N/A
Contractor / Bid-Vendor:	N/A
Contractor / Bid-Vendor:	N/A
Contractor / Bid-Vendor:	N/A
Construction Manager / GC:	N/A
CM/GC PROJECT MANAGER:	N/A
Design Professional:	N/A

REPORT DATE, PREPARED BY: **7/29/2019** Janssen Gingras

ADMINISTRATIVE OVERVIEW:

Total # of Bid-Vendors:	1
# of OSD/MBE/SBE Bid-Vendors:	0
# of Local Bid-Vendors:	1
\$ Value of OSD/MBE/SBE Participation:	\$ -
\$ Value of Local Participation:	\$ 189,348.76

PROJECT DESCRIPTION:

Scope of Work:

Remove existing car stops. Mill and level existing asphalt. Sweep and haul off millings. Pave new parking lot. Stripe parking lot to include all directional arrows, parking spaces, handicap parking, etc. Reinstall car stops.

OSD/MBE/SBE PARTICIPATION REGISTRATION:

OSD/HCPS

State of Florida

County List:

City List:

Other List:

CONSTRUCTION UPDATE:

TYPE	% COMP.	REMARKS
Site	100%	Mill and Pave Parking
Finishes	100%	Stripe Parking
N/A	0%	N/A
N/A	0%	N/A
N/A	0%	N/A

PROGRESS PENDING ISSUES (& RESPONSIBILITIES):

Current Critical Issues:

Issue	Responsibility

CONTRACT STATUS:

CURRENT CONTRACT AMOUNT:	\$	189,348.76
AMOUNT BILLED TO DATE:	\$	189,348.76
PERCENT DOLLARS EXPENDED:		100%
CONTRACT CALENDAR DAYS:		76
CALENDAR DAYS EXPENDED:		76
PERCENT TIME EXPENDED:		100%
TOTAL LOST WEATHER DAYS:		8

COMMENTS:
